



Trip Report

SIROMBU NIAS ISLAND

INDONESIA

By:

Frans Sugiarta

June 2006



1. Trip Period:

- 27 June 2006 – 01 July 2006

2. Trip Objective:

- Checking Project Progress (number of houses completed + infrastructure + school)
- Going thru the check list for each completed houses with Kojo's Site manager to control the quality of products.

3. Results

- Houses:
As per 29 of June 2006, the date of my arrival in Sirombu, the total number of houses completed is **239 houses**.





▪ **Infrastructures:**

- Roads are quite done but I was asking Kojo to put some gravel on top so that it will not too dusty, especially for the main road.
- Water installation is done. There are water stations installed at the main road (see picture) and also there are some well-points have been built. Water treatment is working and supplying water to the tower which later distributes water to the complex (see picture).



Water Tower




Water Stations

- Electrical installation for every house also has been completed. Still missing the connection from the main power (government line) to the complex. We have submitted our proposal to the government five months ago but still no realization. We (UID and Kojo) will continue pushing for this matter.



o Septic Tank system has been completed.

DATE : June 21, 2006
MONACO DUPLEXES AND SEPTIC TANK LOCATION

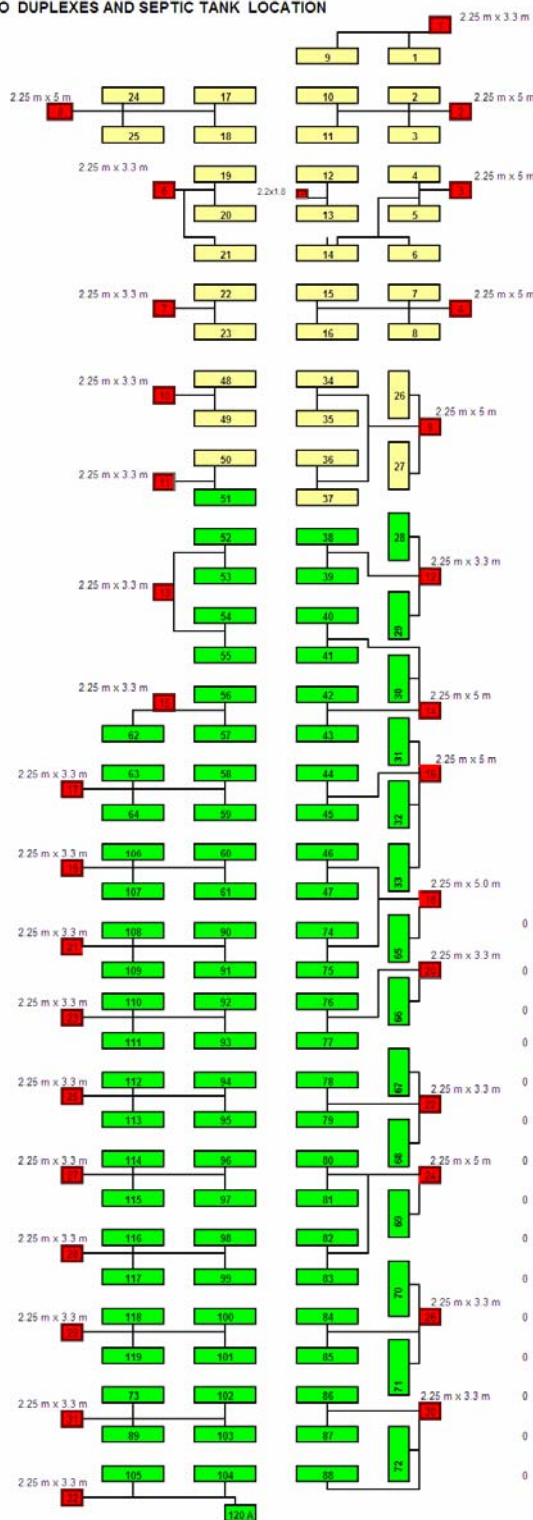

LEGEND :

- Completed and Occupied
- Lock-up Completion
- Ongoing Duplexes and septic tank
- Septic tank location
- Septic tank completed
- Batter board completed
- Water tank installed + squat closet
- Dplx connected to septic tank
- Electrical installation not completed
- Gutter completed

A	Total houses requirement	=	239
B	Total completed to date	=	239
C	Total balance to complete	=	0
D	Total houses occupied	=	68
E	Total houses in-progress	=	0
F	Total houses lock-up todate	=	171



- School Constructions.

As per 29 June 2006, 35% project progress has been achieved. Estimation date of completion is 28 of July 2006.



- House Checklist.

Together with Kojo's project manager, Mr. Bien Clavio, we have gone thru each house to check its quality. There are a few defects has been found and identified during the process and Mr. Clavio has assigned his crew to fix them.



Concrete pad to the bathroom is missing



Defect & Broken Light Switches



Ceiling panel need to be re-nailed



Panel-join need to be fixed



Doors need to be fixed



Missing window Jalousie's



4. Conclusions:

- 239 Houses in Sirombu are completed and accepted.

5. Next Step:

- Handing over the remaining 171 houses to the beneficiaries. Shooting date for this event is 25 of July 2006.
- Coordinating the handover event with our local task force members (Delasiga), local authorities, district government officials and Bureau of Reconstructions & Rehabilitation Aceh-Nias (BRR).
- Controlling the finishing of the school project.
- Reporting to BRR and Department of Education once the school is finished.
- Pushing PLN (Government Electricity Company) for power connections.
- Project's Inauguration ceremony.
- Final report and evaluation.
